
إمكان
IMKAN

AL-AMERAH PHASE 1

Integrated Building Permit & Local Authorities Approval Strategy

MEPS Process • Current Status • Way Forward • AOR Actions

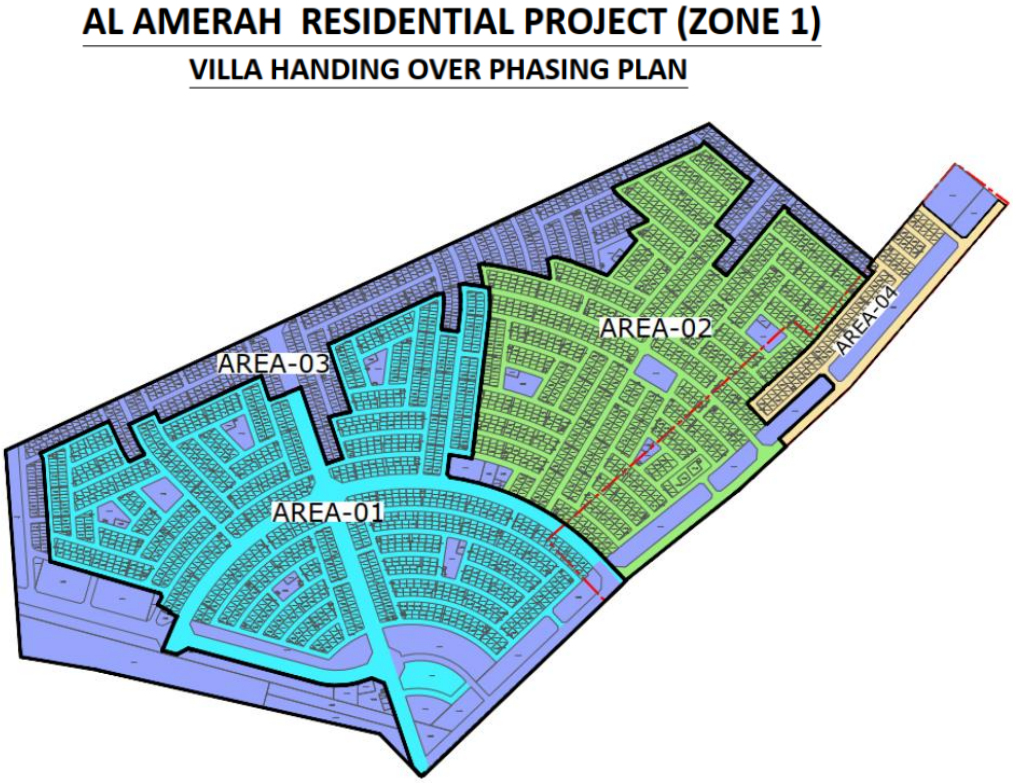

PURPOSE

A consolidated, project-specific strategy for progressing the Al-Amerah Phase 1 Building Permit through MEPS, closing linked authority requirements, and coordinating the AOR's immediate actions.

Role	Responsibility
CLIENT	Provides appointments, decisions, client documents and timely endorsements.
AOR	Owns MEPS/TAMM submissions, authority coordination, comment closure and submission records.

1. Executive Summary

This report consolidates the project-specific Building Permit way-forward strategy with the broader Abu Dhabi permitting and local-authority approval framework. Repeated content has been merged, and general guidance is clearly distinguished from the requirements currently generated for this project in MEPS.

RECOMMENDED PERMITTING ROUTE

Close the pending Site Clearance; upload the obtained EAD approval as the only Step 03A item currently required from our side; monitor MEPS for any additional requirements; and submit the coordinated Architectural, Structural and LDN electrical-distribution packages together at Step 04.

Current project position

Workstream	Status	Immediate implication
EAD, GIS and DCR	**OBTAINED**	Validate scope and validity; maintain conditions in the permit design.
Site Clearance	**PENDING**	AOR to close AAM Roads, TAQA Electricity and ADSCC comments and resubmit.
Estidama	**IN PROCESS**	Appoint the specialist/PQP and progress technical coordination.
Soil report	**IN PROCESS**	Complete for Construction Phase 1 and coordinate with the Step 04 package.
ITC, TAQA and e&/Etisalat	**NOT AVAILABLE**	Progress as permitting-stage workstreams in line with MEPS and authority requirements.
ADCD / fire and life safety	**NOT REQUIRED YET**	Provide only if the MEPS system activates or requests the linked approval.

Strategic objectives

- Maintain one controlled project record, approvals tracker, comment log and submission programme.
- Avoid duplicate preparatory submissions and fragmented authority comments.
- Use one coordinated data set for boundaries, statistics, GIS, utilities, access and environmental commitments.
- Protect the permit programme through early closure of site-clearance and authority dependencies.
- Keep responsibility clear: the AOR is the formal submitting and responding party.

2. Roles, Governance and AOR Scope

Party	Primary responsibilities
CLIENT	Confirm project scope and decisions; provide land/appointment documents; appoint required specialists; endorse authority undertakings; support authority escalations when required.
AOR	Register and manage the project in MEPS/TAMM; prepare and submit applications; coordinate designs and specialists; respond to comments; maintain evidence, trackers and programme; obtain approvals and Building Permit.

AOR permitting responsibilities

- Verify the current MEPS-generated requirement list and record every requirement, owner and target date.
- Review submission packages for alignment with DMT/ADM requirements before upload.
- Lead authority meetings, technical coordination, resubmissions and formal comment closure.
- Issue the authority deliverables matrix to Architecture, Structure, utilities and specialist teams.
- Maintain the live approvals tracker, submission receipts, approval evidence and blocker report.
- Use a permit-readiness gate before Step 04 to confirm package completeness and interface coordination.

GOVERNANCE PRINCIPLE

The AOR is the formal submitting consultant and owns all MEPS/TAMM transactions and authority responses. Authority decisions, additional requirements and review periods remain outside the AOR's control.

Core management records

Record	Minimum content
Approvals tracker	Authority, application number, status, dates, comments, owner, target and evidence link.
Deliverables matrix	Package, document/drawing, responsible discipline, format, revision, due date and approval dependency.
Comment register	Authority comment, response, drawing/document reference, responsible party and closure status.
Risk and action log	Blocker, impact, mitigation, owner, required decision and due date.
AOR dashboard	Overall stage, key approvals, next submission, ageing comments and critical-path actions.

Project controls

The AOR shall use the approved DMP/DCR and valid land information as the permit baseline; maintain one MEPS project record subject to ADM confirmation; and align boundaries, statistics, GIS, utilities, access and approval conditions through one controlled data set.

3. Integrated MEPS Permitting Flow — Steps 01–05

The following sequence is the controlling Building Permit route. Activities may run in parallel, but dependencies and decision gates must be formally managed.

01	PROJECT REGISTRATION Confirm the permit scope and planning basis. Obtain the valid affection/site plan, land information and DMT-format appointment documents. AOR registers the project and verifies the MEPS-generated requirements.
02	SITE CLEARANCE Close the pending Site Clearance application and resolve the authority comments. Site Clearance approval is required before MEPS permits a new Soil Work Permit.
03A	MANDATORY / PREPARATORY Upload the obtained EAD approval. No other submission is required from our side at present unless ADM/MEPS formally activates or requests it.
03B	OTHER PREPARATORY Monitor MEPS. Progress additional NOCs only when required by the system, an authority condition or a permit dependency. No separate Step 03B submission is currently planned.
04	FULL BUILDING PERMIT Preferred route: submit Architecture, Structure and coordinated LDN together, supported by the soil report and applicable approval evidence.
05	DELIVERY APPOINTMENTS After approval, appoint the contractor and site-supervision consultant in MEPS, enter contract information and complete permit issuance / work-start requirements.

PREFERRED DECISION GATE

As this is a development project and key deliverables and approvals—including the Utility Demand (LDN), Soil Report, Geotechnical documentation and Structural drawings—are not yet ready, the AOR shall proceed with the available requirements through the MEPS preparatory stage. Although this is not the preferred route, it is necessary to maintain progress until the outstanding requirements are completed and approved, after which the project can proceed to Step 04.

4. Step 02 — Site Clearance: Current Situation and Strategy

CURRENT STATUS

Site Clearance application B2-SC-A-2026-001625 is pending. The AOR must close the outstanding comments, resubmit and obtain approval before dependent activities progress.

Entity	Current position	AOR action
TAQA Water	**APPROVED**	Retain approval evidence and verify validity.
TAQA Electricity	**MODIFICATION REQUIRED**	Coordinate the comment concerning unavailable infrastructure services; confirm the acceptable authority treatment with TAQA/ADM.
AAM Roads	**PENDING DOCUMENTS**	Submit consultant-signed official undertaking, authorised signatory ID, consultancy commercial licence and power of attorney.
e& / Etisalat (AAM-C)	**MODIFICATION REQUIRED**	Submit the requested architectural site/location plan showing the building coordinates; bilingual building information and area details with an explanatory letter for the proposed addition; and an undertaking to protect e& telecom infrastructure and cables during construction and any future modification.
ADSCC	**REJECTED / INFRASTRUCTURE UNAVAILABLE**	Coordinate with ADSCC and ADM to confirm how the unavailable infrastructure service is to be addressed and documented.

Site Clearance closure strategy

- Compile one complete resubmission set and verify all signatures, authorisations and licence documents before upload.
- Seek written confirmation of the treatment of unavailable TAQA Electricity and ADSCC infrastructure services.
- Record any deferred connection, relocation or protection condition for coordination before the applicable construction activity.
- Follow up through a single authority comment matrix until all linked items are closed.
- Do not programme a new Soil Work Permit before Site Clearance is fully approved, as the current MEPS logic prevents it.

5. Steps 03A and 03B — Project-Specific Treatment

Step 03A — Mandatory and Preparatory Approvals

CURRENT REQUIREMENT

The only submission required from our side under Step 03A at this time is the obtained EAD approval. No other mandatory or preparatory submission is currently required unless ADM/MEPS formally requests or activates it.

- Upload the obtained EAD approval against the applicable mandatory requirement.
- Maintain the EAD conditions through design and construction.
- Monitor the MEPS requirement list after each authority update or resubmission.

- If the Soil Report is not ready, the AOR may submit the available Architectural drawings and coordinated LDN package through the preparatory stage, subject to ADM/MEPS requirements. The Soil Report, geotechnical documents and Structural drawings shall be submitted once completed.

Step 03B — Other preparatory approvals

No separate Step 03B submission is planned at present. GIS and DCR remain part of the approved project basis. Estidama, utility interfaces and other authority requirements will be progressed at the stage identified by MEPS or the applicable approval conditions.

Preparatory-stage requirement	Status	Required action / document to upload
Architectural Drawings	**PENDING**	Obtain the Client-stamped Architectural package together with the applicable ADM forms and submit through MEPS.
Structural Drawings	**NOT READY**	Complete and stamp the Structural drawings following receipt of the Soil Report and geotechnical documentation.
Soil Report / Geotechnical Package	**IN PROCESS**	Obtain the complete Soil Report and geotechnical package, stamped by the appointed Structural Third Party, for uploading to MEPS.
Structural Third-Party Appointment	**IN PROCESS**	The Structural Third Party has been appointed in MEPS; the system appointment remains under process.
EAD Approval	**OBTAINED**	Upload the obtained EAD approval and maintain compliance with its conditions.

Preparatory-stage requirement	Status	Required action / document to upload
ITC Approval	**NOT AVAILABLE**	Complete the traffic/access requirements, obtain ITC approval and upload it through the applicable MEPS route.
TAQA Electical	**NOT AVAILABLE**	Complete the utility-demand calculation and obtain the approved Load Demand Notification (LDN) for submission through MEPS.
e& / Etisalat Approval	**NOT AVAILABLE**	Complete the telecom coordination, obtain the required approval/NOC and upload it to MEPS.
Estidama PCRS	**IN PROCESS**	Complete the Estidama Consultant/PQP appointment, approve the discipline scorecards and upload the required PCRS documents.
ADCD / Fire and Life-Safety Approval	**NOT REQUIRED YET**	No submission is currently required. Provide the approval or supporting evidence only if requested or generated by MEPS.

6. Step 04 — Coordinated Full Building Permit Submission

SUBMISSION DECISION

Submit the Architectural, Structural and coordinated LDN electrical-distribution packages together within the Full Building Permit application, supported by the completed soil report and applicable authority evidence.

Package	Minimum coordinated content
Architecture	Scope worksheet, permit drawings, development statistics, code/compliance information, access and approved authority conditions.
Structure	Drawings, calculations, models, Building Index Form and geotechnical basis, as applicable.
LDN / electrical distribution	Coordinated distribution design, demand/capacity information, interfaces and TAQA supporting information.
Supporting approvals	Obtained EAD, GIS and DCR records; applicable ITC, TAQA, Estidama, telecom and other MEPS-generated evidence.
Linked approvals	ADCD/fire and life safety and other linked approvals only if required by the system for this project.

Why the coordinated Step 04 route is preferred

- The coordinated Step 04 Building Permit submission is preferred because the applicable review KPIs are shorter than those for separate preparatory submissions, supporting faster approval.

- Submitting Architecture, Structure and LDN together also avoids the longer preparatory review route and reduces duplicated submissions and review cycles.

CONTINGENCY — NOT RECOMMENDED

Separate preparatory Architecture and LDN submissions should be used only if ADM specifically directs this route while the soil report is pending. It is not preferred because of the longer review period and repeated comment cycles.

7. Project Approval and Deliverable Status

Status is colour-coded to distinguish what is available, what is in process and what remains to be obtained. Authority items are tracked against the permitting stage; construction deliverables are tracked against the applicable construction phase.

Requirement	Status	Current position	Stage / phase
EAD	OBTAINED	Environmental approval available; maintain its conditions.	Permitting stage
GIS	OBTAINED	GIS submission/coordination completed; keep data aligned.	Permitting stage
DCR	OBTAINED	Approved planning/control basis available.	Permitting stage
Site Clearance	PENDING	Application B2-SC-A-2026-001625 requires comment closure.	Permitting stage
Estidama	IN PROCESS	Specialist/PQP appointment and coordination remain in process.	Permitting stage
Soil report	IN PROCESS	Geotechnical report being prepared.	Construction Phase 1
ITC	NOT AVAILABLE	Traffic/access approval remains to be obtained.	Permitting stage
TAQA Distribution	NOT AVAILABLE	Demand, capacity, tie-in and LDN coordination remain.	Permitting stage
e& / Etisalat	NOT AVAILABLE	Telecom NOC and interface coordination remain.	Permitting stage
ADCD / fire and life safety	NOT REQUIRED YET	Provide only if MEPS activates or requests it.	Conditional

STATUS CONTROL

Before relying on any obtained approval, the AOR must verify its validity, plot/scope coverage and consistency with the current permit design.

8. AOR Action Required and Way Forward

The following actions convert the strategy into an accountable submission plan. The AOR should maintain these actions in the live authority tracker and report progress to the CLIENT.

Priority	AOR action	Required output / closure evidence
1 — Immediate	Close Site Clearance documents and comments.	Complete AAM Roads documentation; written resolution/accepted treatment for TAQA Electricity and ADSCC; approved Site Clearance.
2 — Immediate	Complete and submit stamped Architectural drawings.	Coordinated and stamped Architectural preparatory package submitted in MEPS.
3 — Immediate	Verify the live MEPS mandatory/preparatory list.	Dated system extract and updated approvals tracker confirming EAD as the only current Step 03A submission.
4 — Immediate	Upload/validate EAD approval.	Already Uploaded on the system
5 — Immediate	Confirm Estidama specialist/PQP appointment.	Appointment evidence, responsibility matrix and submission programme.
6 — High	Progress ITC, TAQA and e&/Etisalat workstreams.	Submission route, application references, comment logs and target closure dates.
7 — High	Complete the soil report for Construction Phase 1.	Approved/final geotechnical report aligned with the structural basis.
8 — High	Issue the coordinated permit deliverables matrix.	Architecture, Structure, LDN and specialist package list with owners, revisions and dates.
9 — High	Hold the Step 04 permit-readiness workshop.	Closed interface checklist and authorised submission release.
10 — Ongoing	Monitor conditional linked approvals.	Updated tracker and closure evidence for every MEPS requirement.
11 — Next gate	Prepare the Full Building Permit submission.	Step 04 package released after preparatory requirements are accepted.
12— Post-approval	Complete Step 05 appointments.	Contractor/supervision appointments, contract data and permit/work-start records.

9. Client Decisions, Risks and Controls

Required from CLIENT	Purpose
Confirm the final permit scope, plot/boundary, building list, statistics, access and utility scope.	Establish the controlled Step 04 submission basis.

Required from CLIENT	Purpose
Provide/validate the current affection plan, land documents, DMP/DCR and prior authority conditions.	Complete registration and validate the planning basis.
Sign appointment letters, undertakings and authority forms when required.	Enable the AOR to complete formal submissions and comment closure.
Approve the proposed Estidama Consultant/PQP appointment and the scorecard prepared for each discipline.	To enable the Estidama Consultant/PQP and the relevant disciplines to proceed with the Estidama approval process.
Support escalation on unavailable infrastructure services where authority/client intervention is required.	Resolve TAQA Electricity and ADSCC Site Clearance constraints.
Endorse the coordinated Step 04 route.	Avoid unnecessary preparatory submissions and align the design packages.
Confirm the construction programme interfaces relevant to the permit.	Align authority milestones with construction requirements.

Key risks and controls

Risk	Control
Pending Site Clearance delays dependent activities.	Daily/weekly action tracking; complete resubmission; written authority resolution for unavailable services.
Late specialist or NOC mobilization.	Appointments and submission routes confirmed early; named owners and target dates.
Duplicate preparatory reviews.	Retain Architecture, Structure and LDN for one coordinated Step 04 submission unless ADM directs otherwise.
Approval/drawing inconsistency.	Validity and scope check before reliance; one controlled data set and revision register.
New MEPS-generated requirements.	Recheck the live list after each update; record conditional approvals and immediately assess programme impact.
Handover approvals lag physical completion.	Integrate permitting, NOCs, inspections and as-built clearances into the construction programme.

10. Assumptions and Qualifications

- Final requirements are governed by the approved project documents, the live MEPS-generated requirement list and formal authority directions.
- Authority review periods vary with submission quality, complexity, workload, comment cycles and response time. No fixed duration is guaranteed.
- The affection/site plan must remain valid throughout the relevant registration and submission period.

- The final NOC scope depends on plot location, land status, building use, development scale and available infrastructure networks.
- Obtained approvals must be checked for validity, scope and consistency before being relied upon.
- ADCD/fire and life-safety evidence and any other linked approval will be provided only if requested through MEPS; these are not currently required for this project.
- The precise authority expansion of “LDN” is to be confirmed before external technical submission; this report uses “LDN electrical-distribution package”.
- Any addition-building route under the same MEPS project number remains subject to ADM/MEPS confirmation.

Reference basis

- Project Site Clearance application B2-SC-A-2026-001625 and associated status/comments.
- Current project approval status: EAD, GIS and DCR obtained; Estidama and soil report in process; ITC, TAQA and e&/Etisalat outstanding.
- DMT Building Permit Guidelines and the MEPS/TAMM workflow.
- Approved master planning and DCR documents applicable to Al-Amerah.
- Project-specific permitting strategy and authority records supplied for consolidation.

RECOMMENDED CLIENT ENDORSEMENT

Endorse the integrated permitting strategy and instruct the AOR to close Site Clearance, manage the authority workstreams, complete the permit-readiness gate and proceed with the coordinated Step 04 submission.
